ID	ER	BI	Task Name	Lead Manager	% Work Complete	Start	Finish
1	2237	SD410	Metro-Post St. tie--replace cable phase 1	Cummins	0%	Mon 06-29-09	Wed 09-02-09
2	2464	SD802	LIB12F3 Fix #6 Copper	Cummins	100%	Mon 03-02-09	Fri 05-01-09
3	2487	WD904	KET12F2 Upgrade Columbia Cedar	Cummins	0%	Mon 08-31-09	Fri 11-20-09
4	2253	XS900 XS901	System - Upgrade Meters--Warden and Westside Note: not including Hotsprings as primarily BPA	Magruder	10%	Mon 05-11-09	Thu 10-01-09
5	2467	KS800 KS801	Burke 115 kV Protection and Metering	Magruder	10%	Mon 05-11-09	Thu 10-15-09
6	2420	LT815	Dry Creek--North Lewiston 230kV Reinsulate	James	100%	Fri 02-20-09	Tue 03-10-09
7	2264	PD637 PS401	Terre View 115Sub--Construct (WSU)	Magruder	100%	Fri 01-02-09	Tue 03-31-09
8	2302	PS202 AMT24	Plummer Sub Rebuild	Magruder	60%	Fri 01-02-09	Wed 07-15-09
9	2307	CT906	Idaho Road Transmission	James	100%	Mon 03-02-09	Fri 04-10-09
10	2307	CD900 CS500	Idaho Road 115 kV Substation Note: the distribution portion of this project is 95% complete	Magruder	40%	Fri 01-02-09	Tue 09-01-09
11	2318	LS503	Grangeville 115 Install 15 MVAR Cap Bank	Magruder	90%	Fri 01-02-09	Wed 07-15-09
12	2360	LS635	Lolo 230kV--Rebuild 230kV Yard	Magruder	30%	Fri 01-02-09	Fri 11-20-09
13	2478	KS900 KD900	O'Gara Sub--Transformer Upgrade	Magruder	0%	Mon 08-03-09	Wed 11-18-09

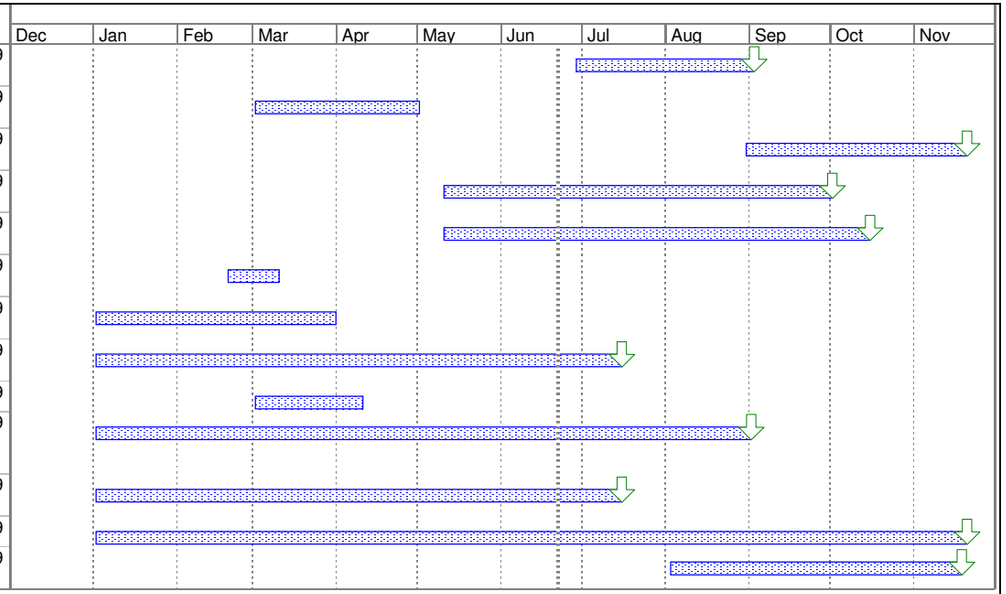

Project: 2009 Top Ten Electrical Proje
Date: Mon 06-22-09

Task
Progress
Baseline
Milestone
Baseline Milestone
Summary
Rolled Up Task
Rolled Up Milestone
Baseline Summary
Rolled Up Baseline
Rolled Up Baseline Milestone
Rolled Up Progress
Split
Baseline Split
External Tasks
Project Summary
Group By Summary
Deadline
