Large Generator Interconnection

Thursday, January 10, 2008

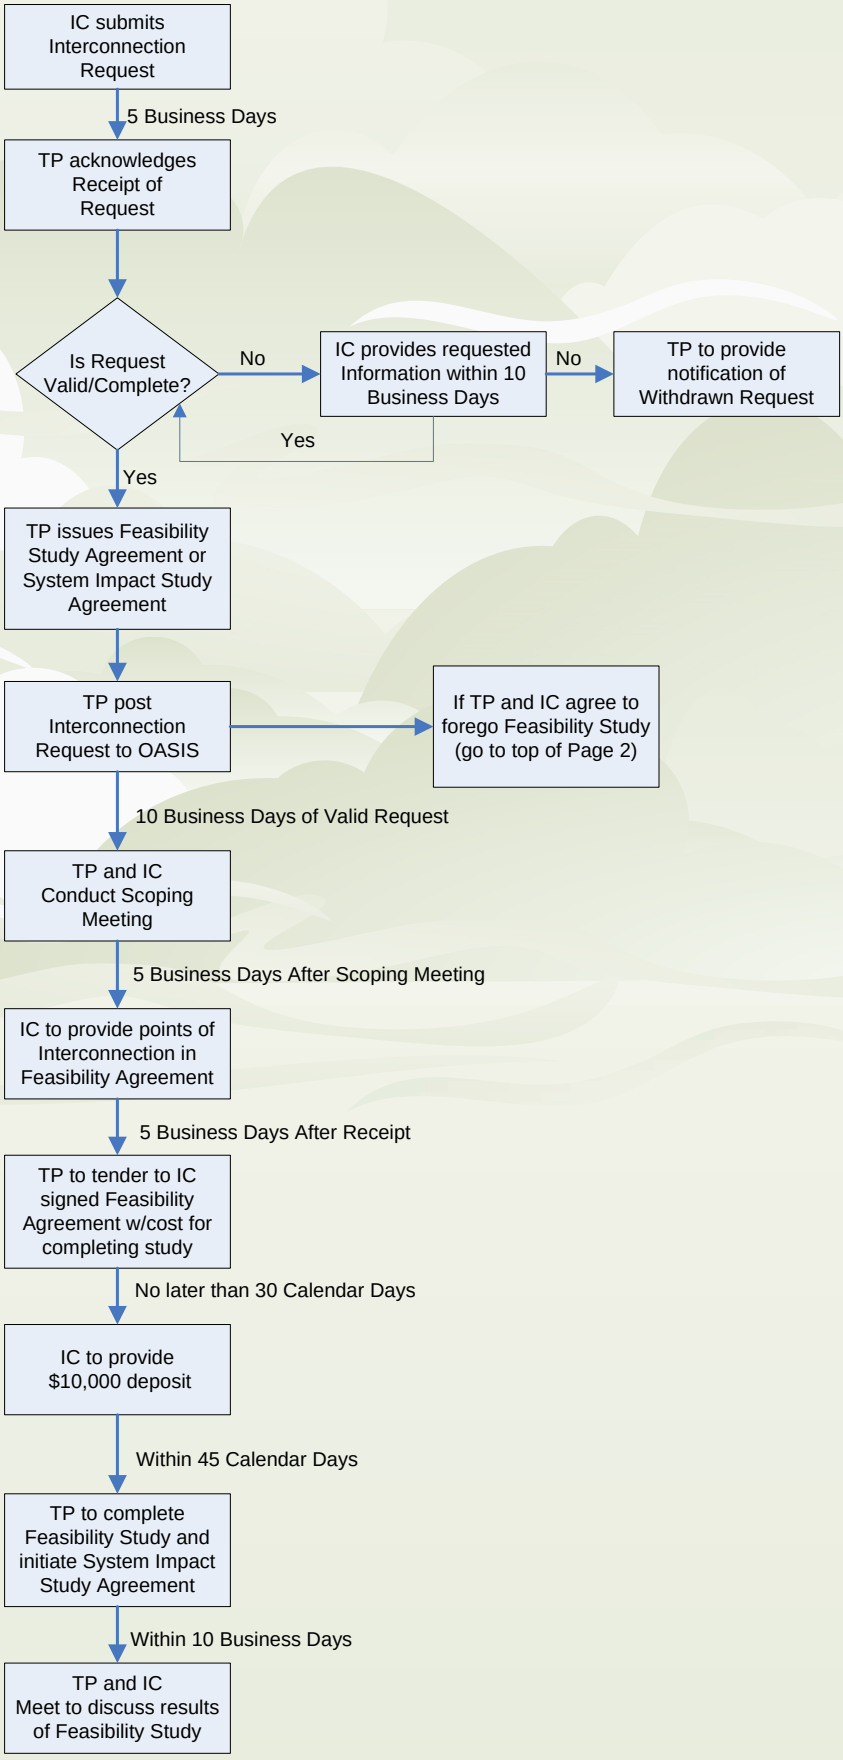

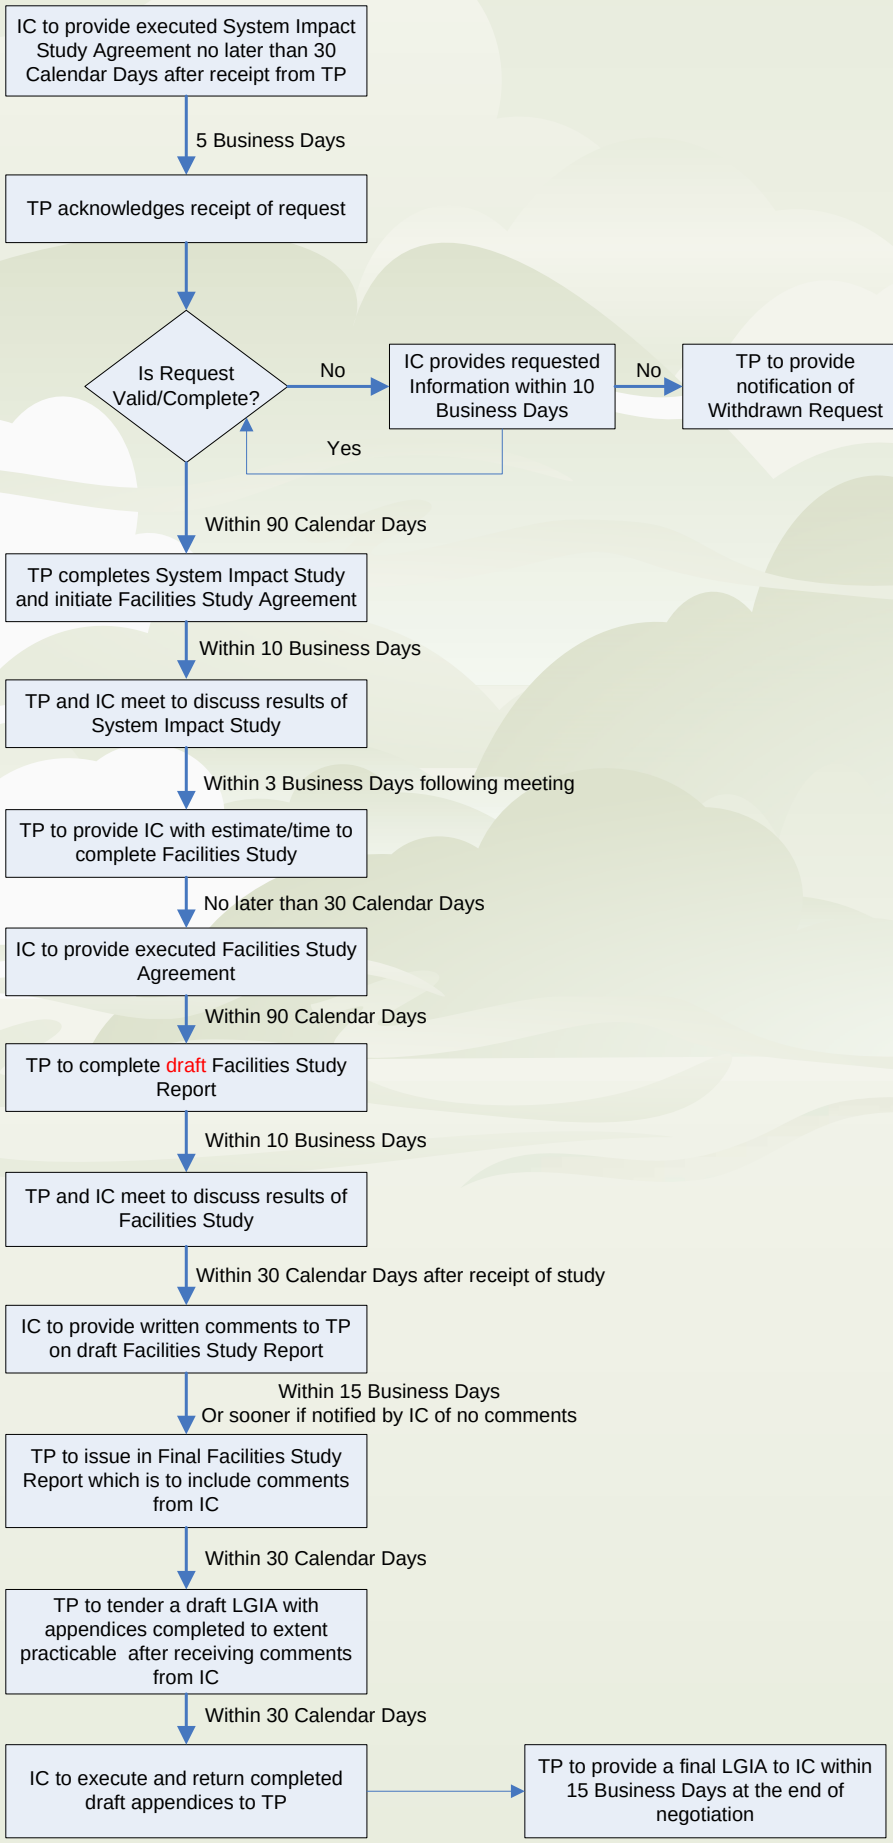
IC to provide executed System Impact Study Agreement no later than 30 Calendar Days after receipt from TP
5 Business Days
TP acknowledges receipt of request
Is Request Valid/Complete?
No
IC provides requested Information within 10 Business Days
No
TP to provide notification of Withdrawn Request
Yes
Within 90 Calendar Days
TP completes System Impact Study and initiate Facilities Study Agreement
Within 10 Business Days
TP and IC meet to discuss results of System Impact Study
Within 3 Business Days following meeting
TP to provide IC with estimate/time to complete Facilities Study
No later than 30 Calendar Days
IC to provide executed Facilities Study Agreement
Within 90 Calendar Days
TP to complete draft Facilities Study Report
Within 10 Business Days
TP and IC meet to discuss results of Facilities Study
Within 30 Calendar Days after receipt of study
IC to provide written comments to TP on draft Facilities Study Report
Within 15 Business Days
Or sooner if notified by IC of no comments
TP to issue in Final Facilities Study Report which is to include comments from IC
Within 30 Calendar Days
TP to tender a draft LGIA with appendices completed to extent practicable after receiving comments from IC
Within 30 Calendar Days
IC to execute and return completed draft appendices to TP
TP to provide a final LGIA to IC within 15 Business Days at the end of negotiation
